


MONTHLY PROGRESS REPORT – UW Campus Wireless Upgrade Project - 5-11-2020



TOTAL AP REFRESH PROGRESS - 47% Complete

Watch



OVERALL SCORE
3.0/5.0

MONTHS UNTIL WRAP-UP
8

Projected Project WRAP-UP DATE:
Q4 2020


ITEMS NEEDING ESCALATION:

- Significant timeline implications with COVID-19 pandemic orders
- Project re-evaluation meeting needed to align on timelines, expectations and outstanding items across the teams.
- Potential difficulty with finance to get more AP's as lead time planning is hampered by COVID-19

OVERVIEW

The Field Services team has fully restarted the delivery of designs to make sure that Westphal continues to have work. They have delivered 8 new designs this month, after working to get back on campus and begin some of their normal work. The expectation at this point is to target the delivery of all designs by the end of June, which is 2 months off the original expectation. There are 27 designs left to be delivered for wiring. At that point, the project will shift to focus completely on the install of AP's on all buildings. I believe that, given the delay due to COVID and the transition we will be looking at from designs to AP installation, it is important that the entire project team meet to discuss the next steps, timeline, expectations and project delivery.

AP Install Information

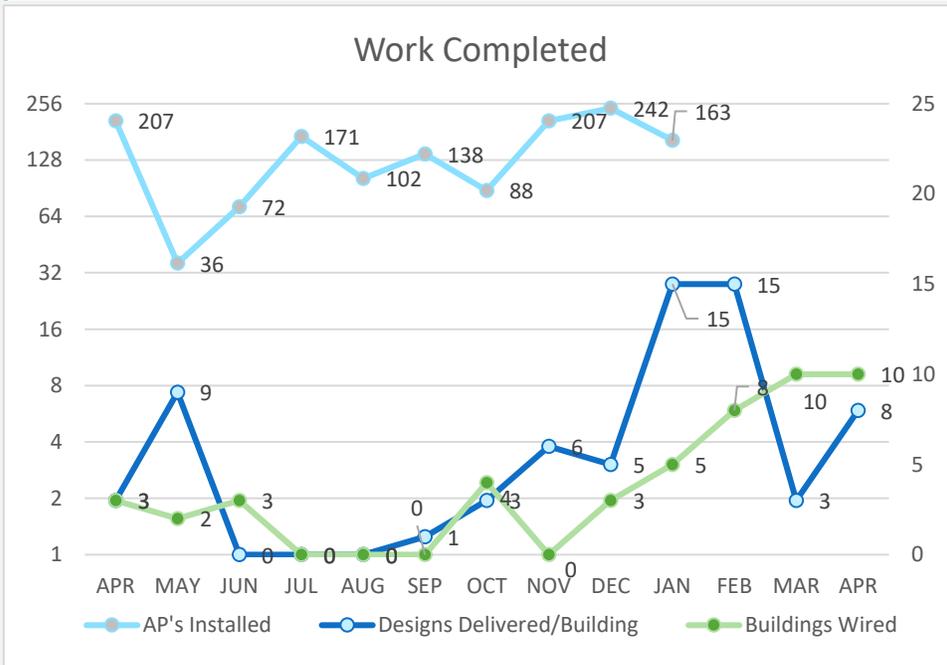

KEY PROGRESS

Field Services Buildings Completed: (0)

Buildings in Progress for AP Install (0)

New Designs Delivered (8)

- Chemistry
- Bascom Hall
- Ingraham Hall
- Babcock Hall
- 0122 Walnut St. Greenhouse
- Goodnight Hall
- 702 West Johnson
- Russell Lab

Electric Shop Completed: (10)


- Enzyme Institute
- Service Building
- Bock Labs
- Nut Sci
- Observatory Hill Office Bld
- Music Hall
- Rust Shreiner Halls
- Livestock Lab
- Poultry lab
- Env. Health and Safety

Electric Shop/Westphal in Progress (7)

Notes:

- **Completed 0 building for a total of 0 AP's installed in February.**
- Westphal and Electric Shop full steam ahead with wiring.
- Field Services restarted designs in full –
- Need to reevaluate timeline given pandemic situation.

Overall AP Installation Progress



**TOTAL AMOUNT OF AP'S INSTALLED
3163 OUT OF 6792 = 47% INSTALLED**
