

MONTHLY PROGRESS REPORT – UW Campus Wireless Upgrade Project - 5-6-2021



TOTAL AP REFRESH PROGRESS - 79% Complete

Improved



OVERALL SCORE
4.0/5.0

MONTHS UNTIL WRAP-UP
2

Projected Project WRAP-UP DATE:
June 30, 2021

POTENTIAL ISSUES/CONCERNS:


- None at this time

OVERVIEW

April was another productive month for this project. The infrastructure team is finishing up the final building (Memorial Library) and is targeted to be completed early this month, which will conclude the infrastructure involvement of this project. That will leave the AP installations for Field Services as the remaining items as we move towards the project wrap-up date of June 30th. Field Services completed installing AP's at 5 buildings for a total of 499 AP's. They are also continuing to cutover buildings, do the final inspections, and otherwise ensure completion. At this point, they have all the AP's and switches necessary to complete this project and believe we are on track for the completion date of June 30th, if nothing abnormal derails the continued progress.

AP Install Information

Work Completed

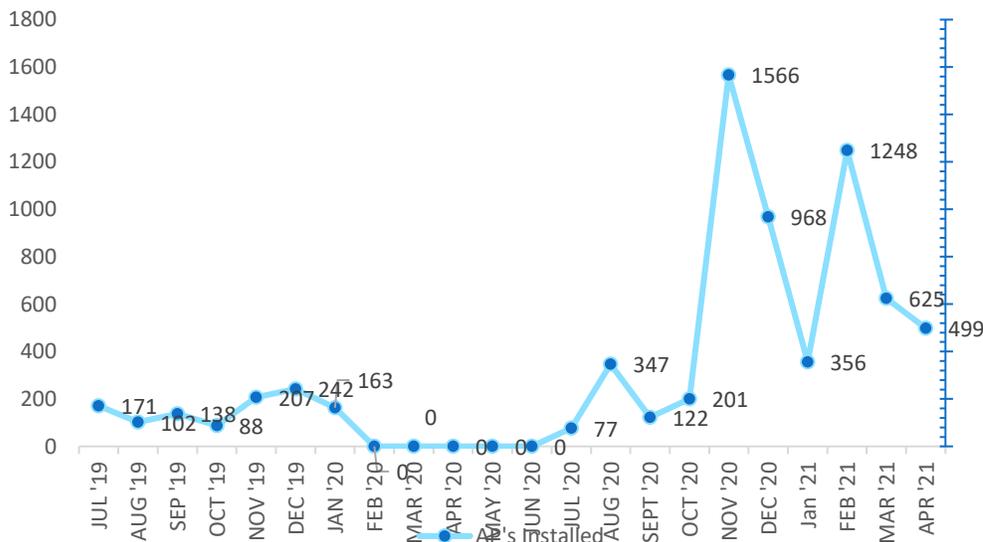


KEY PROGRESS

AP's Deployed (499)

- Hiram Smith Hall
- Mechanical Engineering
- Smith Annex
- MFCOB
- Rust Schreiner Halls

Overall AP Installation Progress

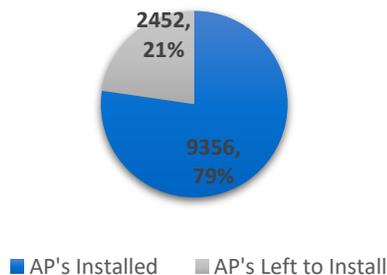

Notes:

- **Deployed new AP's in 5 buildings for a total of 499 AP's installed in March.**
- Electric shop 1 remaining building for wiring:
 - o Memorial Library – **Projected completion later this month.**
- All switches and AP's are on hand for finishing the project.

**TOTAL AMOUNT OF AP'S INSTALLED
9,356 OUT OF 11,808 = 79% INSTALLED**
