


# MONTHLY PROGRESS REPORT – UW Campus Wireless Upgrade Project - 4-3-2020



TOTAL AP REFRESH PROGRESS - 47% Complete

Watch



OVERALL SCORE  
3.5/5.0

MONTHS UNTIL WRAP-UP  
10

Projected Project WRAP-UP DATE:  
Q4 2020


### ITEMS NEEDING ESCALATION:

- Significant timeline implications with COVID-19 pandemic orders

### OVERVIEW

While progress was made in designs in the first half of March, the design work was obviously delayed with the response to the COVID-19 pandemic. Work from home mandates and further precautions to avoid the spread of the illness forced much of the Field Services team to work from home. During this time they have been focusing on prep for potential upcoming deployments and working from floor plans as much as possible to make progress on designs. The absence of students has allowed Westphal and the Electric Shop to make great progress working through many buildings that will be fully ready for deployment when possible. Field services will be evaluating when it can return to campus work after network leadership determines the best course of action.

### AP Install Information

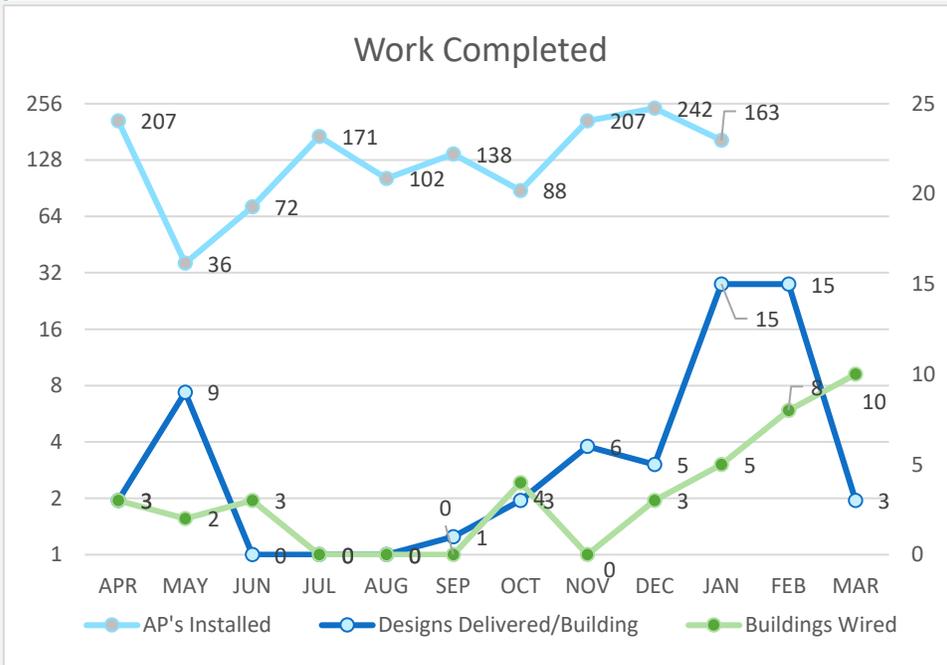

### KEY PROGRESS

Field Services Buildings Completed: (0)

Buildings in Progress for AP Install (0)

New Designs Delivered (3)

- Lathrop Hall
- Waisman
- Safety

Electric Shop Completed: (10)


- Gen Bio
- Animal Science
- 45 N. Charter St
- Hiram Smith Hall
- Hiram Smith Annex
- 30 N Mills
- Service Building Annex
- 1910 Linden Dr.
- Fleet Garage
- Radio Hall

Electric Shop in Progress (10)

### Notes:

- Completed 0 building for a total of 0 AP's installed in February.
- Westphal and Electric Shop full steam ahead with wiring.
- In a situation right now to only respond to emergency services and support key infrastructure given Evers order.
- Gary going to check Westphal and see if they can validate building designs to some degree to assist Field Services.
- May need to reevaluate timeline given Pandemic situation.

### Overall AP Installation Progress



**TOTAL AMOUNT OF AP'S INSTALLED  
3163 OUT OF 6792 = 47% INSTALLED**
