

MONTHLY PROGRESS REPORT – UW Campus Wireless Upgrade Project - 4-9-2021



TOTAL AP REFRESH PROGRESS - 68% Complete

Watch



POTENTIAL ISSUES/CONCERNS:

- None at this time

OVERALL SCORE

4.0/5.0

MONTHS UNTIL WRAP-UP

4

Projected Project WRAP-UP DATE:


June 30, 2021

OVERVIEW

The month of March saw the Field Services team deploy 625 AP's at 9 buildings. Alongside the AP deployments, the Field Services team has continued to fully cut-over buildings, which is the final step after AP's are deployed. The infrastructure team remains on track for finishing the final buildings (Whimer, Microbial, Memorial, Ingraham) by the end of May, with MSE being available to the Field Services team for AP deployment this week. Additional switches have been ordered and are being installed as necessary in the buildings, though more switches may be necessary as Field Services continues to inventory the remaining need. Overall, we continue to make consistent progress towards the expected completion date with no major roadblocks at this point.

AP Install Information

Work Completed

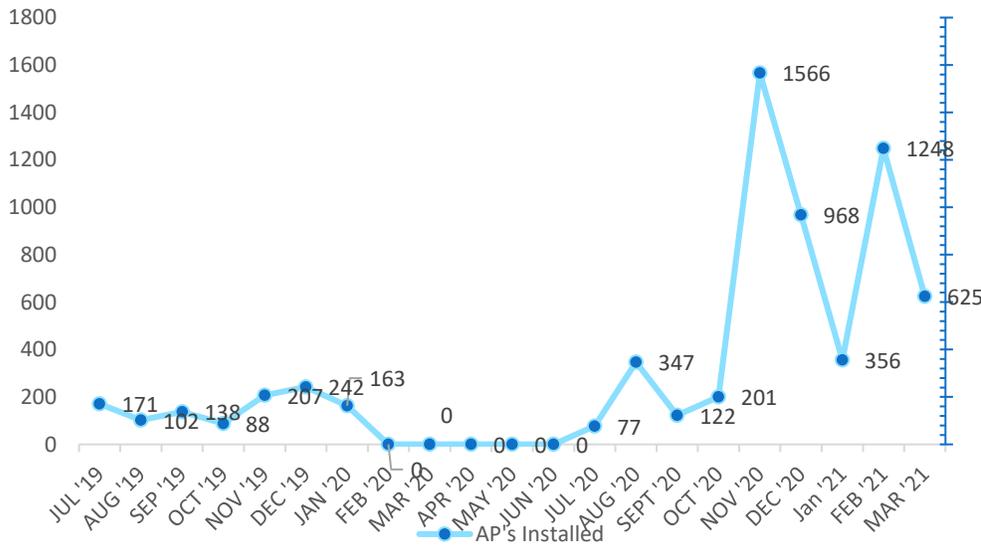


KEY PROGRESS

AP's Deployed (625)

- Mechanical Engineering
- Moore Hall
- Washburn Observatory
- 21 N. Park St
- Observatory Hill Office Building
- Nutritional Science
- Psychology
- Extension Building
- Lathrop

Overall AP Installation Progress

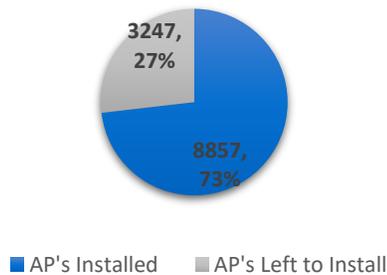

**TOTAL AMOUNT OF AP'S INSTALLED
8857 OUT OF 12104 = 73% INSTALLED**

Notes:

- **Deployed new AP's in 9 buildings for a total of 625 AP's installed in March.**
 - o Electric shop 4 remaining buildings for wiring:
 - Microbial
 - Memorial
 - Whimer
 - Ingraham
 - o Continuing inventory evaluation of switches
