


MONTHLY PROGRESS REPORT – UW Campus Wireless Upgrade Project - 6-3-2020



TOTAL AP REFRESH PROGRESS - 47% Complete

Watch



OVERALL SCORE
3.0/5.0

MONTHS UNTIL WRAP-UP
TBD

Projected Project WRAP-UP DATE:
TBD


ITEMS NEEDING ESCALATION:

- Potential difficulty with finance to get more AP's as lead time planning is hampered by COVID-19
 - o Need to provide Dennis with AP rollout plan for budgetary discussions
- Potential timeline concerns with AP installs and building access
 - o Need to give proper lead time accounting for building access

OVERVIEW

We held a project group meeting on May 27th to realign expectations and reset our planning after the delays caused by the COVID Safer at Home orders and campus closures. We are back to mostly full speed as we target the end of June for the delivery of all buildings designs. After the building designs are delivered, we will be moving into AP installation, focusing on lab and common spaces, as classrooms will be lowest priority given there will be no fall classes. We need to provide a detailed deployment plan to give to Dennis so that he has the information to take to the budgetary committees to ensure we can purchase more AP's in a timely manner for our plan. Gary is working with his team to create that plan as we approach AP deployment phase.

AP Install Information

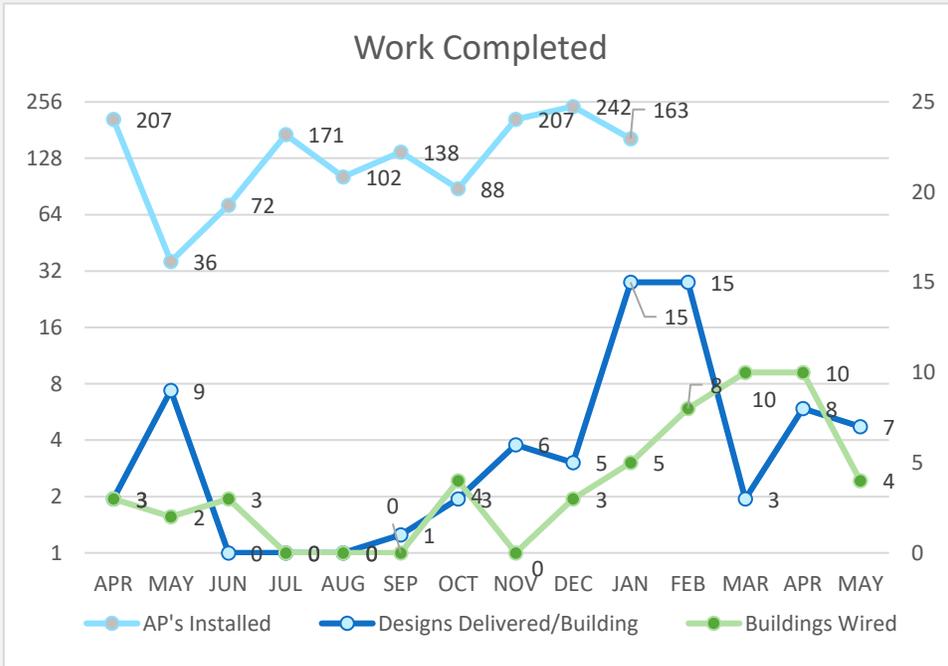

KEY PROGRESS

Field Services Buildings Completed: (0)

Buildings in Progress for AP Install (0)

New Designs Delivered (7)

- Memorial Library
- Biotron
- Science Hall
- Birge Hall
- Computer Aided Engineering
- 432 East Campus Mall
- Engineering Research Bld

Electric Shop Completed: (4)


- Law Bld
- 445 Henry Mall
- Lathrop Hall
- Waisman

Electric Shop/Westphal in Progress (10)

Notes:

- Completed 0 building for a total of 0 AP's installed in May.
- Had a productive project planning meeting on May 27
 - o Less than 30 buildings left for designs
 - End of June target for completion
 - o Building audit planned with Gary and Neil
 - o Gary and Neil to reconcile buildings and get estimates to Westphal for resourcing.
 - o Field Services team to work on deployment plan for Dennis to order AP's

Overall AP Installation Progress



**TOTAL AMOUNT OF AP'S INSTALLED
3163 OUT OF 6792 = 47% INSTALLED**
