

# MONTHLY PROGRESS REPORT – UW Campus Wireless Upgrade Project - 12-4-2020



## TOTAL AP REFRESH PROGRESS - 45% Complete

### Status: Good



OVERALL SCORE  
**4.0/5.0**

MONTHS UNTIL WRAP-UP  
6.75

Projected Project WRAP-UP DATE:  
**June 30, 2021**

### POTENTIAL ISSUES/CONCERNS:

- Heightened sensitivity to install presence with students/faculty returning to campus
- Potential slowdown with low stock of AP's and mounts as we wait for new shipments.
- Ongoing community spread of COVID and potential outages relating to illness.

### OVERVIEW

We have continued a concentrated push for AP deployments this month, with Westphal leading the deployment of new AP's and the Field Services team doing the unboxing and configuring of the new AP's. We had a month of great progress of AP deployment with this division of labor, deploying new AP's in 25 buildings for a count of 1566 new AP's deployed. The Electric Shop is working on wiring the remaining large buildings, which means we will be shifting our focus of new AP deployments on the smaller buildings, with the Field Services team continuing the unboxing and provisioning of new AP's and Westphal doing the new deployments in the smaller buildings.

### AP Install Information

Work Completed



### KEY PROGRESS

#### AP's Deployed (1566)

Animal Science	AOSS
Mcardle Cancer Research Bld.	Sterling Hall
Ag Hall	Nut Sci
King Soils and Greenhouse	Goodnight Hall
Stock Pavilion	Biochemistry Bld.
Washburn Observatory	Biochemistry Labs
432 East Campus Mall	Nielson Tennis
Russell Labs	Biochemical Sciences
Extension Building	Moore Hall
Bascom Hall	Science Hall
Harlow Primate Lab	Law Bld
Primate	Chamberlin Hall
1220 Capital Court	30 N Mills

#### Westphal AP building deployments prioritization list (11)


- Ingraham Hall
- WISCPIC
- School of Social Work
- Lathrop Hall
- 702 W. Johnson
- Babcock Hall
- Material Science and Engineering
- Computer Aided Engineering
- Birge Hall
- ECB
- Limnology

#### Notes:

- **Deployed new AP's in 25 buildings for a total of 1566 AP's installed in November.**

- o New order for AP's placed and being delivered.
- o Electric shop continuing to wire larger buildings.

### Overall AP Installation Progress

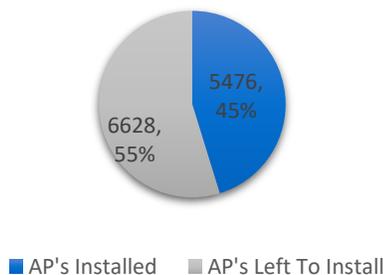

**TOTAL AMOUNT OF AP'S INSTALLED  
5476 OUT OF 12104 = 45% INSTALLED**
