

MONTHLY PROGRESS REPORT – UW Campus Wireless Upgrade Project - 2-5-2021



TOTAL AP REFRESH PROGRESS - 57% Complete

Watch



POTENTIAL ISSUES/CONCERNS:

- Heightened sensitivity to install presence with students/faculty returning to campus
- Ongoing community spread of COVID and potential outages relating to illness.

OVERALL SCORE
3.5/5.0

MONTHS UNTIL WRAP-UP
TBD


Projected Project WRAP-UP DATE:
June 30, 2021

OVERVIEW

As we ramp back up after the holidays with the new year we are continuing unboxing of the large AP order that arrived at the end of the year, and prepping the AP's for Westphal to continue their progress of AP installs. There was a dip in New AP deployments do to ramping back up and unboxing efforts of AP stock but 4 buildings were finished for a total of 356 new AP's, and there are 8 buildings in progress for another 779 new AP's that are expected to finish in the next week or two. The Field Services team is continuing to make their way through the buildings after Westphal to do building reviews and finalize building prep for AP transitions. Infrastructure continues to make great progress on wiring with only a few more large buildings left for wiring.

AP Install Information

Work Completed

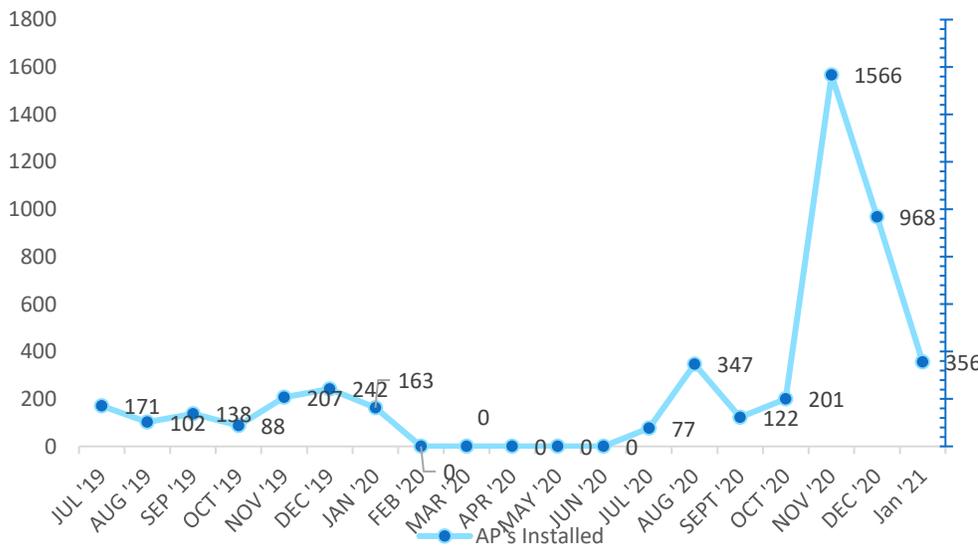

KEY PROGRESS


AP's Deployed (356)

- Pharmacy
- AHBS
- Service Building

Westphal AP building deployments prioritization list (8)

- Babcock Hall
- Ingraham Hall
- 21 N. Park
- Gen Bio
- Service Building Annex
- MFCOB
- Engineering Research Building
- Mechanical Engineering
- 630 W. Mifflin
- Chemistry
- SMI

Overall AP Installation Progress



■ AP's Installed ■ AP's Left to Install

Notes:

- **Deployed new AP's in 4 buildings for a total of 356 AP's installed in January.**
 - o Infrastructure working on finishing wiring by end of February
 - o 21 North Park on hold due to COVID testing

**TOTAL AMOUNT OF AP'S INSTALLED
6984 OUT OF 12104 = 57% INSTALLED**
