


MONTHLY PROGRESS REPORT –UW Campus Wireless Upgrade Project - 12-5-2019



TOTAL AP REFRESH PROGRESS - 41% Complete

Watch



OVERALL SCORE

3.0/5.0

MONTHS UNTIL WRAP-UP

8

Projected Project WRAP-UP DATE:

Q2 2020


ITEMS NEEDING ESCALATION:

- Establish regular meeting with Westphal, Field Services and Electric shop for deployment planning

OVERVIEW

The project team met on November 19th to discuss what has been working with the project, what can be improved and how we can adjust and plan for new delivery expectations. The overall feedback was very positive from the team, after speaking with Gary, and they have already incorporated the date fields we mentioned in their reporting sheet, to provide better visibility in AP install times. We are still working through some of the suggestions we had at the November 19th meeting, including establishing a 30 minute bi-weekly meeting with Westphal, Field Services and Electric shop to outline and plan the upcoming two weeks of work and to ensure effective communication across the teams.

AP Install Information

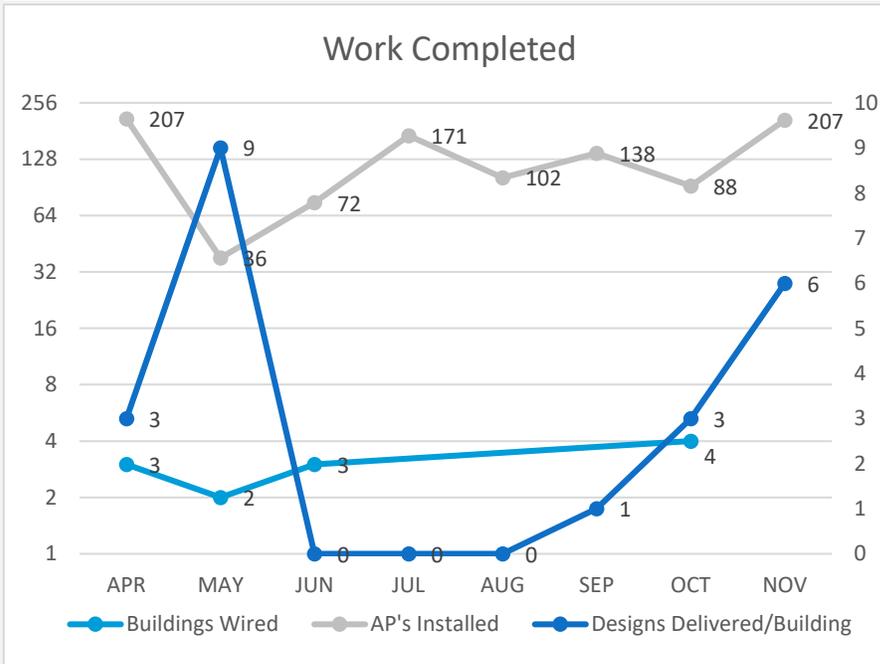

KEY PROGRESS

Field Services Buildings Completed: (3)

- Steenbock Library
- Red Gym
- Stovall Hall

Buildings in Progress for AP Install

- Van Hise
- Limonology
- HC White Library

New Designs Delivered (6)

- AHBS
- Animal Sciences
- Human Ecology
- King-Soils
- Steenbock Library
- Stovall Hall

Electric Shop Completed: (0)


Electric Shop in Progress

- HSLC
- Social Science
- Limnology
- Pyle Center
- Ag Hall
- King Soils and Greenhouse

Notes:

- Completed 3 buildings for a total of 207 AP's installed in November.
- Field Services Team has added date fields to Excel sheet, focused on prepping the smaller academic spaces for holiday deployments and began to improve integration across the team with newer members
- Added additional switches to Van Hise and are scheduling with current occupants to complete.
- School of Human Ecology additional switches installed and scheduling out with current occupants.
- Design out for Gen bio and waiting for confirmation from building manager

Overall AP Installation Progress



**TOTAL AMOUNT OF AP'S INSTALLED
2758 OUT OF 6792 = 41% INSTALLED**
