

MONTHLY PROGRESS REPORT – UW Campus Wireless Upgrade Project - 3-5-2021



TOTAL AP REFRESH PROGRESS - 68% Complete

Watch



POTENTIAL ISSUES/CONCERNS:

- Heightened sensitivity to install presence with students/faculty returning to campus
- Ongoing community spread of COVID and potential outages relating to illness.

OVERALL SCORE

4.0/5.0

MONTHS UNTIL WRAP-UP

4

Projected Project WRAP-UP DATE:


June 30, 2021

OVERVIEW

The month of February saw (1248 AP's deployed at 16 buildings). AP unboxing and configuration was completed in February by the Field Services team and they are now working on deployments as well as patching and cut overs of buildings with all AP's installed. Field Services is also assisting with the switch review and count to ensure we have enough switches and provide order information to Dennis, as necessary. The Electric Shop is continuing their progress of wiring in the 5 remaining buildings with a still expected completion date of the end of May.

AP Install Information

Work Completed

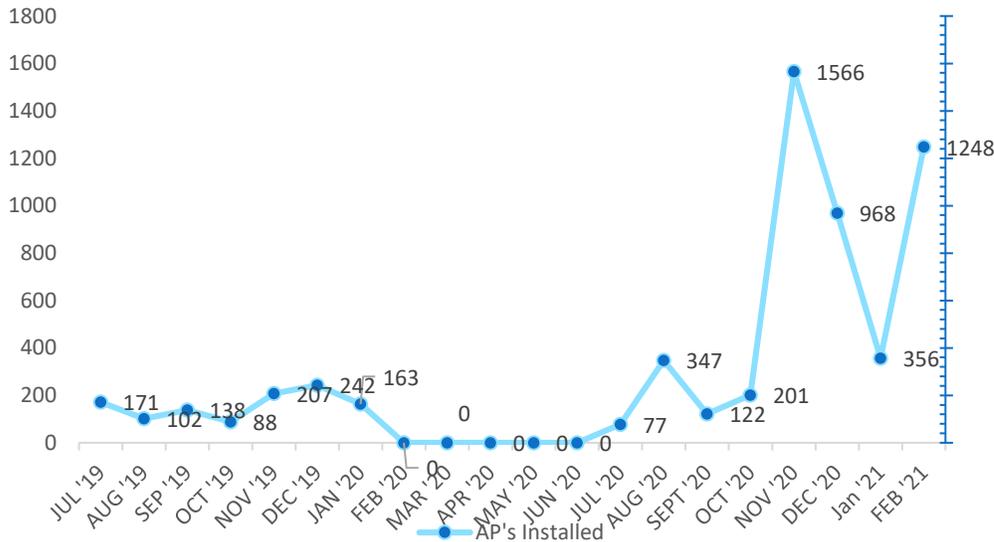

KEY PROGRESS

AP's Deployed (1248)

- Chemistry
- 630 W. Mifflin
- Service Building
- 21 North Park
- GenBio
- Service Building
- Service Building Annex
- MFCOB
- Engineering Research
- Mechanical Engineering
- SMI
- Biotron
- Animal Science
- Primate
- Chamberlain Hall
- Sterling Hall


AP building deployments prioritization list (9)

- Arts Loft
- 432 ECM
- 1220 Capitol Court
- Harlow
- Goodnight Hall
- Extension building
- Russell Labs
- 432 N. Murray
- East Campus Mall

Notes:

- **Deployed new AP's in 16 buildings for a total of 1248 AP's installed in February.**
 - o Electric shop 5 remaining buildings for wiring:
 - 333 East
 - MSE
 - Memorial
 - Whimer
 - Union
 - o Working on getting Switch count to order switches

Overall AP Installation Progress



■ AP's Installed ■ AP's Left to Install

**TOTAL AMOUNT OF AP'S INSTALLED
8232 OUT OF 12104 = 68% INSTALLED**
